



# Executive Steering Committee (ESC) Update

## Minnesota Eligibility Technology System (METS)

Greg Poehling | Director – Program Management Division, MNIT Services @  
DHS/MNsure

August 8, 2017

08/08/2017

MNsure's Accessibility & Equal Opportunity (AEO) office can provide this information in accessible formats for individuals with disabilities. Additionally, the AEO office can provide information on disability rights and protections to access MNsure programs. The AEO office can be reached via 1-855-3MNSURE (1-855-366-7873) or [AEO@MNsure.org](mailto:AEO@MNsure.org).

- Fall Release
  - Open Enrollment Readiness
- Winter Release
- 2018 Roadmap Planning
- Roadmap & Project Overviews
- Detailed Project Status Update

- MMIS Interface (Includes Redesign)
- Notices (Includes Redesign)
- Carrier Integration
  - EDI Fixes & Enhancements, Phase 1 1095-A Reporting with Enrollment Caps
- Trigger of Failure to Reconcile (FTR) via Federal Hub
- Defects

- MMIS Interface (Includes Redesign)
- Notices (Includes Redesign)
- Carrier Integration
- Periodic Data Match / FTI Masking
- Defects

# 2018 Roadmap Planning

1. **Identify and score new proposed project work\***
2. **Determine capacity, define project scope and gather Level of Effort (LOE) for proposed 2018 projects and ongoing efforts\***
3. Rank and prioritize projects (Blueline)
4. Identify Release timeframe
5. PMT Recommendation
6. ESC Approval (September)

**\* Work on these items already underway**

# METS 2017 Release Roadmap

|                            |
|----------------------------|
| Work Incomplete            |
| Work Completed             |
| Work Currently Underway    |
| <b>XL</b> = "Mega Project" |


| Spring 2017                                    | Summer 2017                                   | Fall 2017                          | Winter 2017                            |
|--|---|------------------------------------|--|
| Assister Portal                                | Cúram Eligibility System Upgrade <b>XL</b>    | MMIS Interface (Includes Redesign) | MMIS Interface (Includes Redesign)     |
| Notices (Includes Redesign)                    | Supervisor Workspace / Org Location Structure | Notices (Includes Redesign)        | Notices (Includes Redesign)            |
| PRISM Defects                                  | Notices (Includes Redesign)                   | Carrier Integration                | Carrier Integration                    |
| Cost Sharing                                   | MMIS Interface (Includes Redesign)            | Trigger of FTR via Federal Hub     | Periodic Data Match (PDM) /FTI Masking |
| Federal Poverty Level (FPL) - MA Annual Update | Defects                                       | Defects                            | Defects                                |
| MMIS Interface (Includes Redesign)             |   |                                    |  |
| Defects  |   |                                    |  |

Ongoing Efforts

|                                      |
|--------------------------------------|
| 1095-A Operations                    |
| 1095-B Operations                    |
| Data Access and Management - Reports |
| Infrastructure Improvements          |
| MAXIS to METS Migration              |
| Premium Reconciliation               |
| Periodic/Annual Work                 |
| Renewals Operations                  |


|                         |
|-------------------------|
| Work Incomplete         |
| Work Completed          |
| Work Currently Underway |
| Work On Hold            |

# 2017 Carrier Integration Project Roadmap

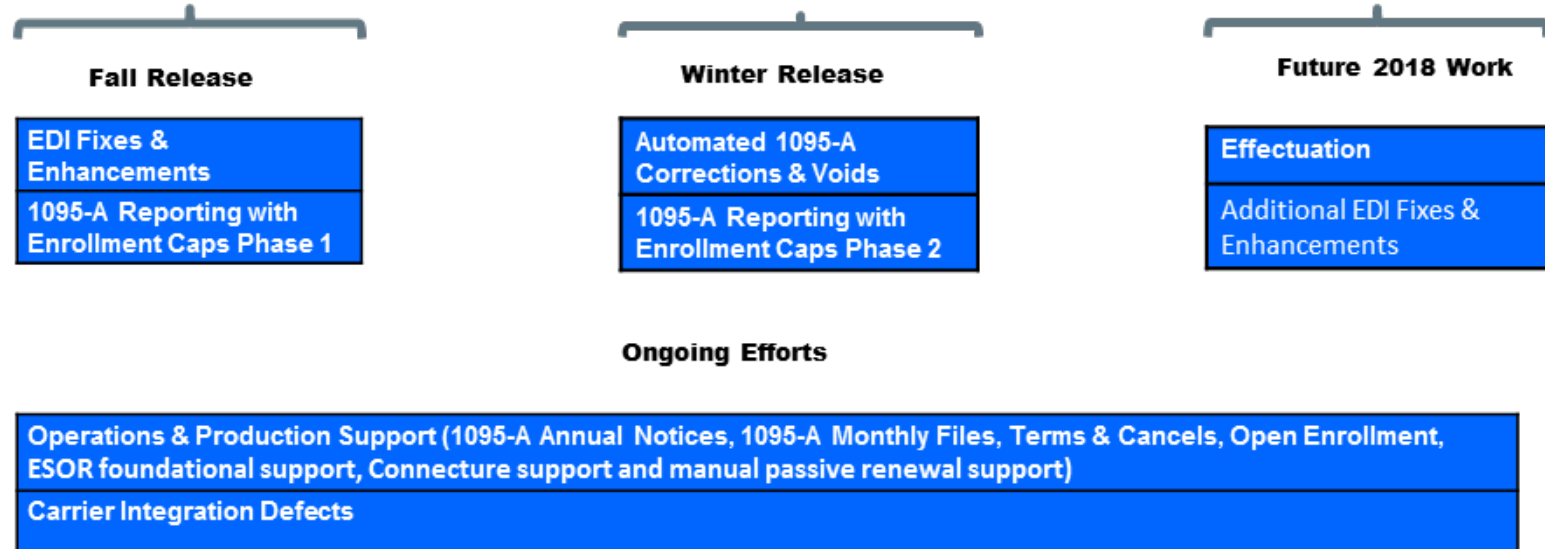

# IT Release Plan: Public Program Work— Ongoing Efforts

|                            |
|----------------------------|
| Work Incomplete            |
| Work Completed             |
| Work Currently Underway    |
| <b>XL</b> = "Mega Project" |

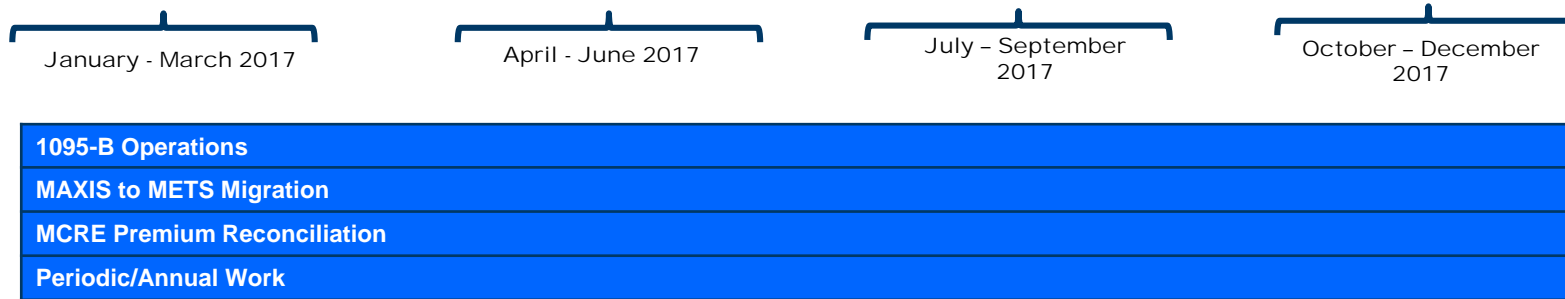



# Program Status

| Project Name                            | Release          | Scope | Schedule | Issues | Risk   | Overall |
|---|------------------|-------|----------|--------|--------|---------|
| Trigger of FTR via Federal Hub          | 17.3 Fall 2017   | Green | Yellow   | Green  | Green  | Yellow  |
| Defects 17.3                            | 17.3 Fall 2017   | Green | Green    | Green  | Green  | Green   |
| Notices 17.3                            | 17.3 Fall 2017   | Green | Green    | Green  | Green  | Green   |
| Periodic Data Match / FTI Masking       | 17.4 Winter 2017 | Green | Green    | Green  | Green  | Green   |
| 1095-A Operations                       | Ongoing          | Green | Green    | Green  | Green  | Green   |
| 1095-B Operations                       | Ongoing          | Green | Green    | Green  | Red    | Red     |
| Carrier Integration                     | Ongoing          | Green | Green    | Green  | Green  | Green   |
| Data Access & Management (Reports)      | Ongoing          | Green | Green    | Green  | Green  | Green   |
| Infrastructure Improvements             | Ongoing          | Green | Yellow   | Yellow | Yellow | Yellow  |
| MAXIS to METS Migration                 | Ongoing          | Green | Green    | Green  | Green  | Green   |
| MCRE Premium Reconciliation             | Ongoing          | Green | Green    | Green  | Green  | Green   |
| MMIS Interface (Includes Redesign)      | Ongoing          | Green | Yellow   | Yellow | Green  | Yellow  |
| Periodic / Annual Work                  | Ongoing          | Green | Yellow   | Green  | Yellow | Yellow  |
| <b>METS Program Status as of 8/4/17</b> |                  |       |          |        |        |         |
